



September 12, 2022

RE: 12" Water Main Extension

Dover Residents- Please see the current construction schedule update for the 12" water main extension:

Construction on the City of Dover water main extension is anticipated to commence with clearing and grubbing on September 12th. The bike trails will be closed as of this date (9/12).


Clearing and grubbing will take approximately 3 working days.

September 16th will begin with the installation of the water main piping. The watermain installation is expected to take approximately 3 weeks.

On or around October 10th, we will begin restoration on the field and installation of BMP's on the steep slope, taking approximately 3 days.

With the approval of the restoration from the engineer/landowner, we will begin hydroseeding and mulching with approved grasses. Demobilization of equipment will occur at the same time, on or around October 17th.

Please see the map below for trail closures:

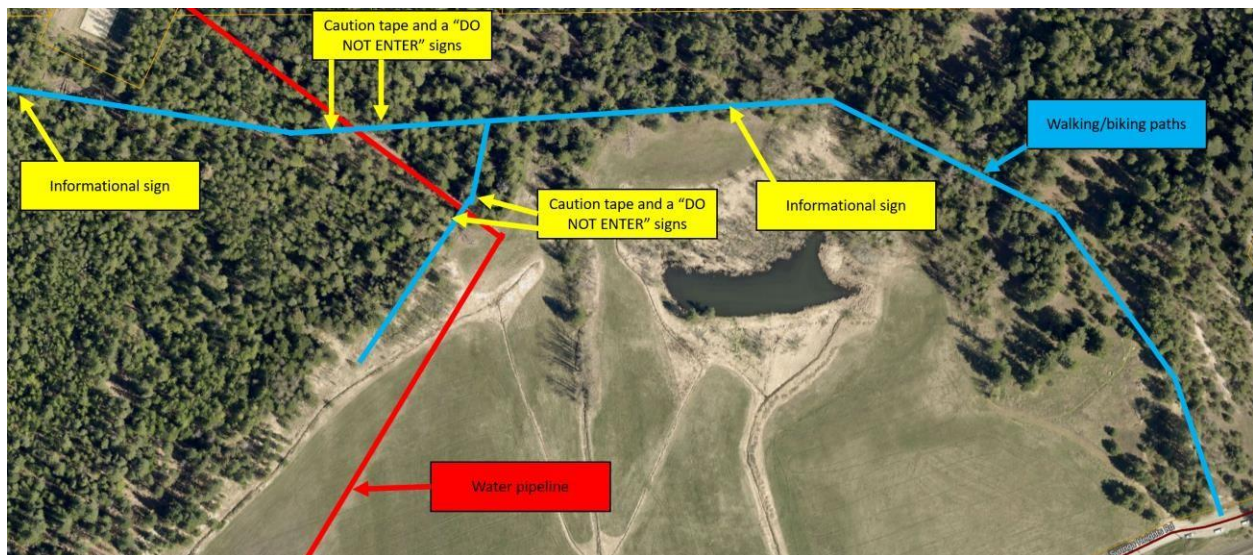

P.O. Box 115, 699 Lakeshore Ave., Dover, ID 83825

Phone: 208-265-8339

<https://cityofdover.id.gov>
